Mainframe Software Portfolio Roadmap - Example

Generated: 2026-11-06 12:27 PM Eastern Standard Time
By: seanz

DECISION PATH All workstreams and owners

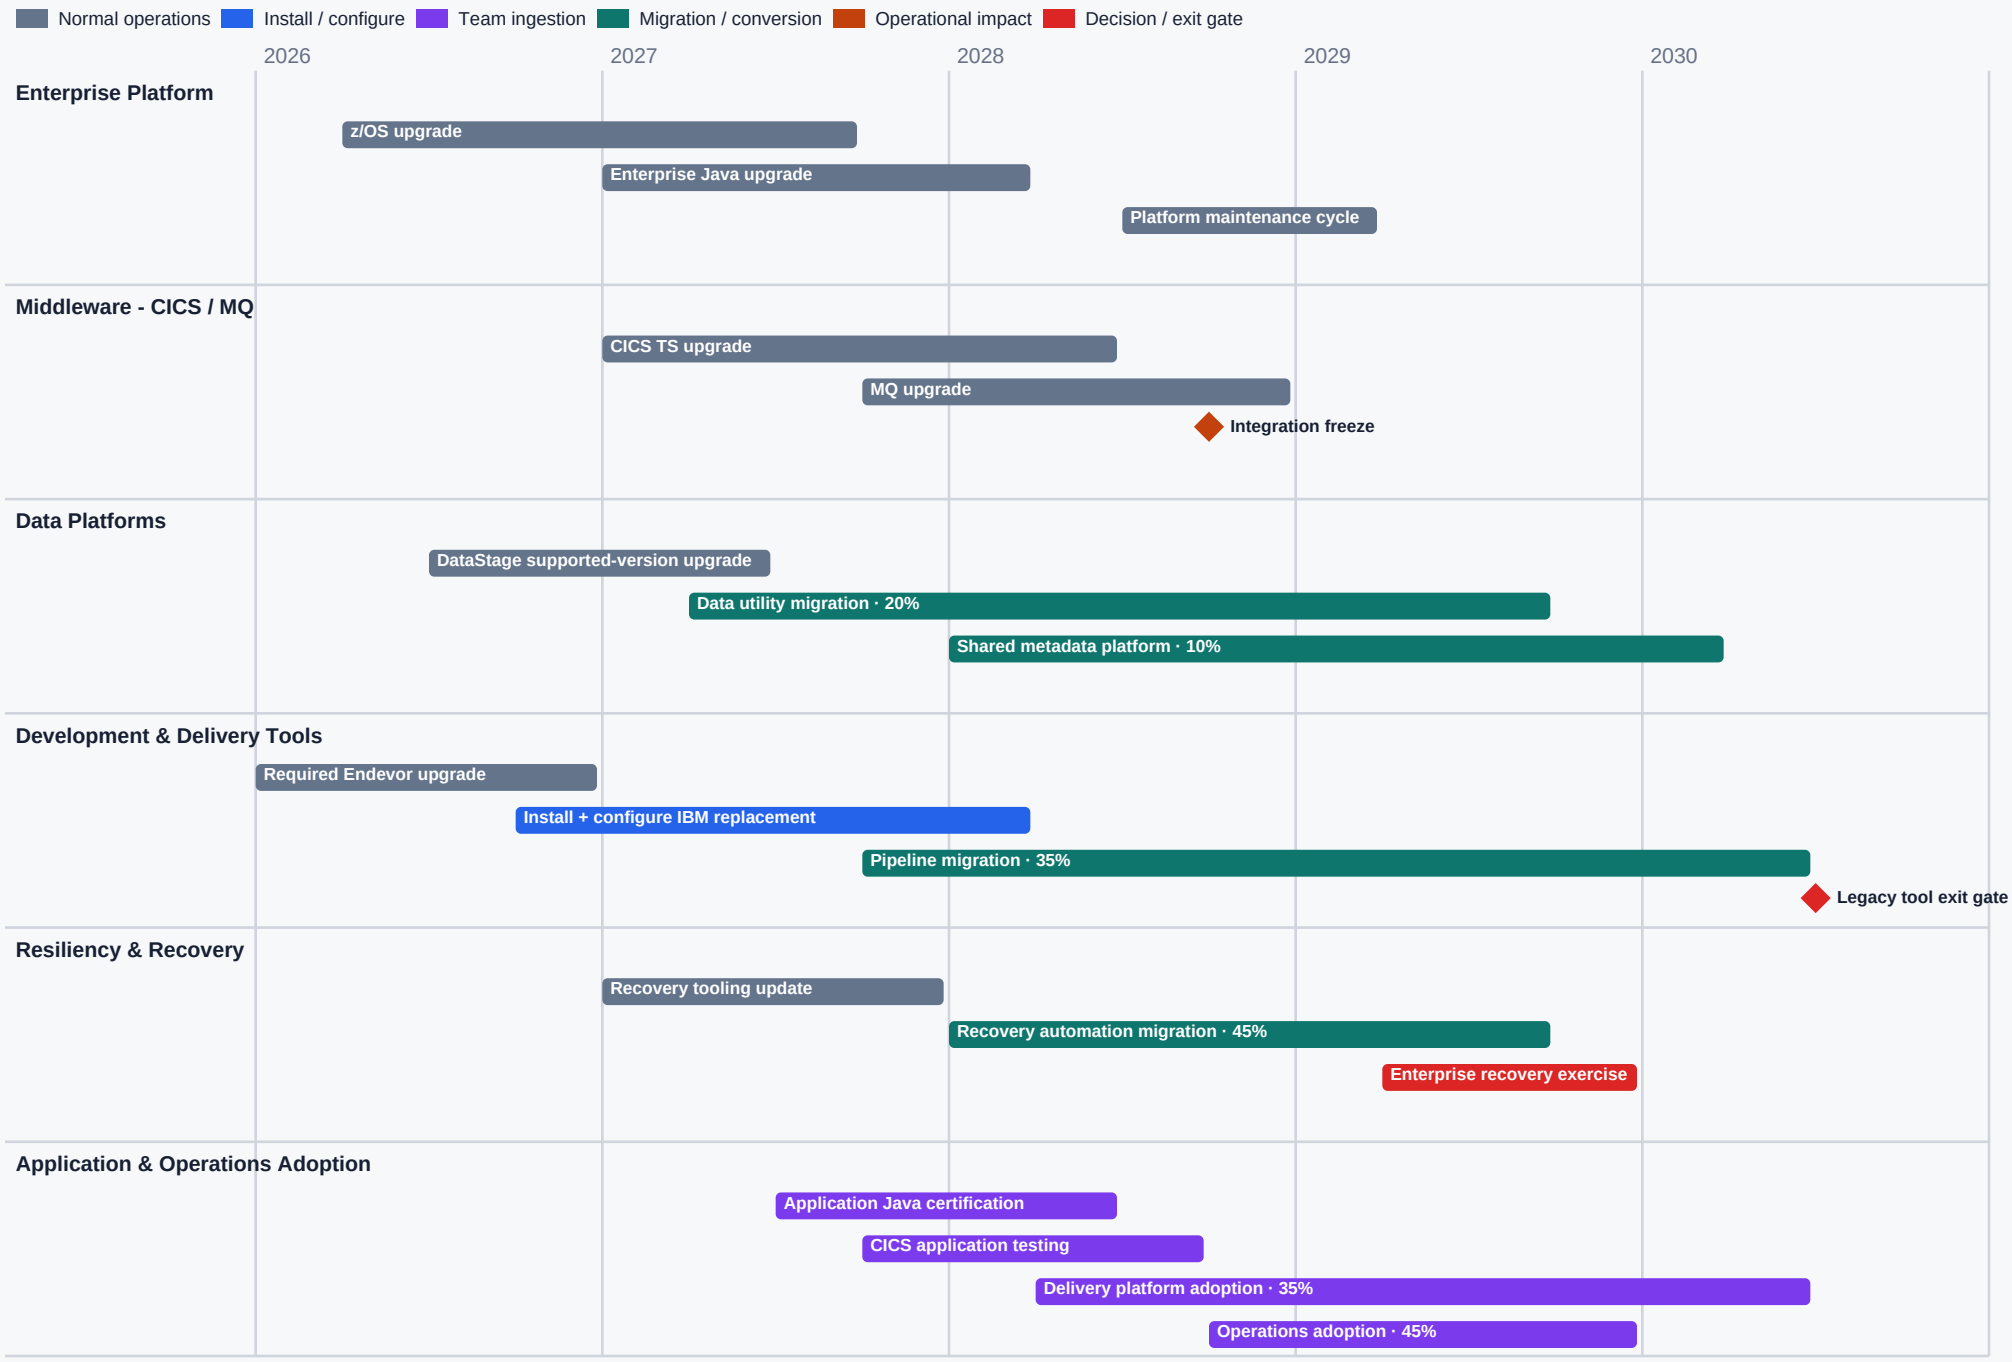

Decision-path view 1 - Only entries active for this path are shown.

Theme: executive

Path Details

Generated: 2026-11-06 12:27 PM Eastern Standard Time
By: seanz

DECISION PATH All workstreams and owners

- **2026-2027 | Development & Delivery Tools | Normal operations | Required Endevor upgrade**
  Keep the existing product supported while the replacement platform is being prepared.
- **2026.25-2027.75 | Enterprise Platform | Normal operations | z/OS upgrade**
  Illustrative foundation upgrade. Owner: Alex. Ingesting team: Platform Engineering. Downstream testing affects CICS, MQ, Java, and delivery tools.
- **2026.5-2027.5 | Data Platforms | Normal operations | DataStage supported-version upgrade**
  Normal version upgrade required while longer-term data modernization is planned.
- **2026.75-2028.25 | Development & Delivery Tools | Install / configure | Install + configure IBM replacement**
  System Programming installs, secures, integrates, and validates the target delivery platform.
- **2027-2028.25 | Enterprise Platform | Normal operations | Enterprise Java upgrade**
  Java runtime uplift with application certification. Overlaps the latter portion of the z/OS upgrade and middleware testing.
- **2027-2028.5 | Middleware — CICS / MQ | Normal operations | CICS TS upgrade**
  CICS upgrade and application certification. Shares testing windows with Java and the delivery-tool migration.
- **2027-2028 | Resiliency & Recovery | Normal operations | Recovery tooling update**
  Mandatory update to preserve support and recovery readiness.
- **2027.25-2029.75 | Data Platforms | Migration / conversion | Data utility migration · 20%**
  Illustrative migration from a current data utility to its target platform. Progress: 20%.
- **2027.5-2028.5 | Application & Operations Adoption | Team ingestion | Application Java certification**
  Application teams test and certify workloads on the new Java runtime.
- **2027.75-2029 | Middleware — CICS / MQ | Normal operations | MQ upgrade**
  MQ infrastructure upgrade. Illustrates a second middleware effort overlapping CICS, Java, and resiliency changes.
- **2027.75-2030.5 | Development & Delivery Tools | Migration / conversion | Pipeline migration · 35%**
  Application pipelines and operational processes move to the IBM replacement. Progress: 35%.
- **2027.75-2028.75 | Application & Operations Adoption | Team ingestion | CICS application testing**
  Application testing overlaps Java certification and delivery-tool onboarding.
- **2028-2030.25 | Data Platforms | Migration / conversion | Shared metadata platform · 10%**
  Joint Broadcom and Data dependency. The work overlaps delivery-tool migration and application adoption. Progress: 10%.
- **2028-2029.75 | Resiliency & Recovery | Migration / conversion | Recovery automation migration · 45%**
  Migration and configuration of recovery automation. Progress: 45%.

Path Details (continued)

Generated: 2026-11-06 12:27 PM Eastern Standard Time
By: seanz

DECISION PATH All workstreams and owners

2028.25-2030.5 | Application & Operations Adoption | Team ingestion | Delivery platform adoption · 35%
Application Development adopts the replacement delivery platform. Progress: 35%.

2028.5-2029.25 | Enterprise Platform | Normal operations | Platform maintenance cycle
Normal maintenance that consumes capacity during tool migration and resilience work.

Decision at 2028.75 | Middleware — CICS / MQ | Operational impact | Integration freeze
Example restricted-change window during combined CICS and MQ cutover activity.

2028.75-2030 | Application & Operations Adoption | Team ingestion | Operations adoption · 45%
Operations adopts recovery automation, monitoring, procedures, and support ownership. Progress: 45%.

2029.25-2030 | Resiliency & Recovery | Decision / exit gate | Enterprise recovery exercise
Formal exercise validating the new automation while other migrations are still active.

Decision at 2030.5 | Development & Delivery Tools | Decision / exit gate | Legacy tool exit gate
Decision gate for retiring the prior delivery utility before contract end.

Written flow for the decision path shown above.
