Mainframe SDLC Modernization Roadmap

Generated: 2026-09-15 08:16 AM Eastern Daylight Time
By: Mainframe Engineering

DECISION PATH Contract Path: Early renewal: 2027-2029 | Selected SDLC Solution: IBM suite viable

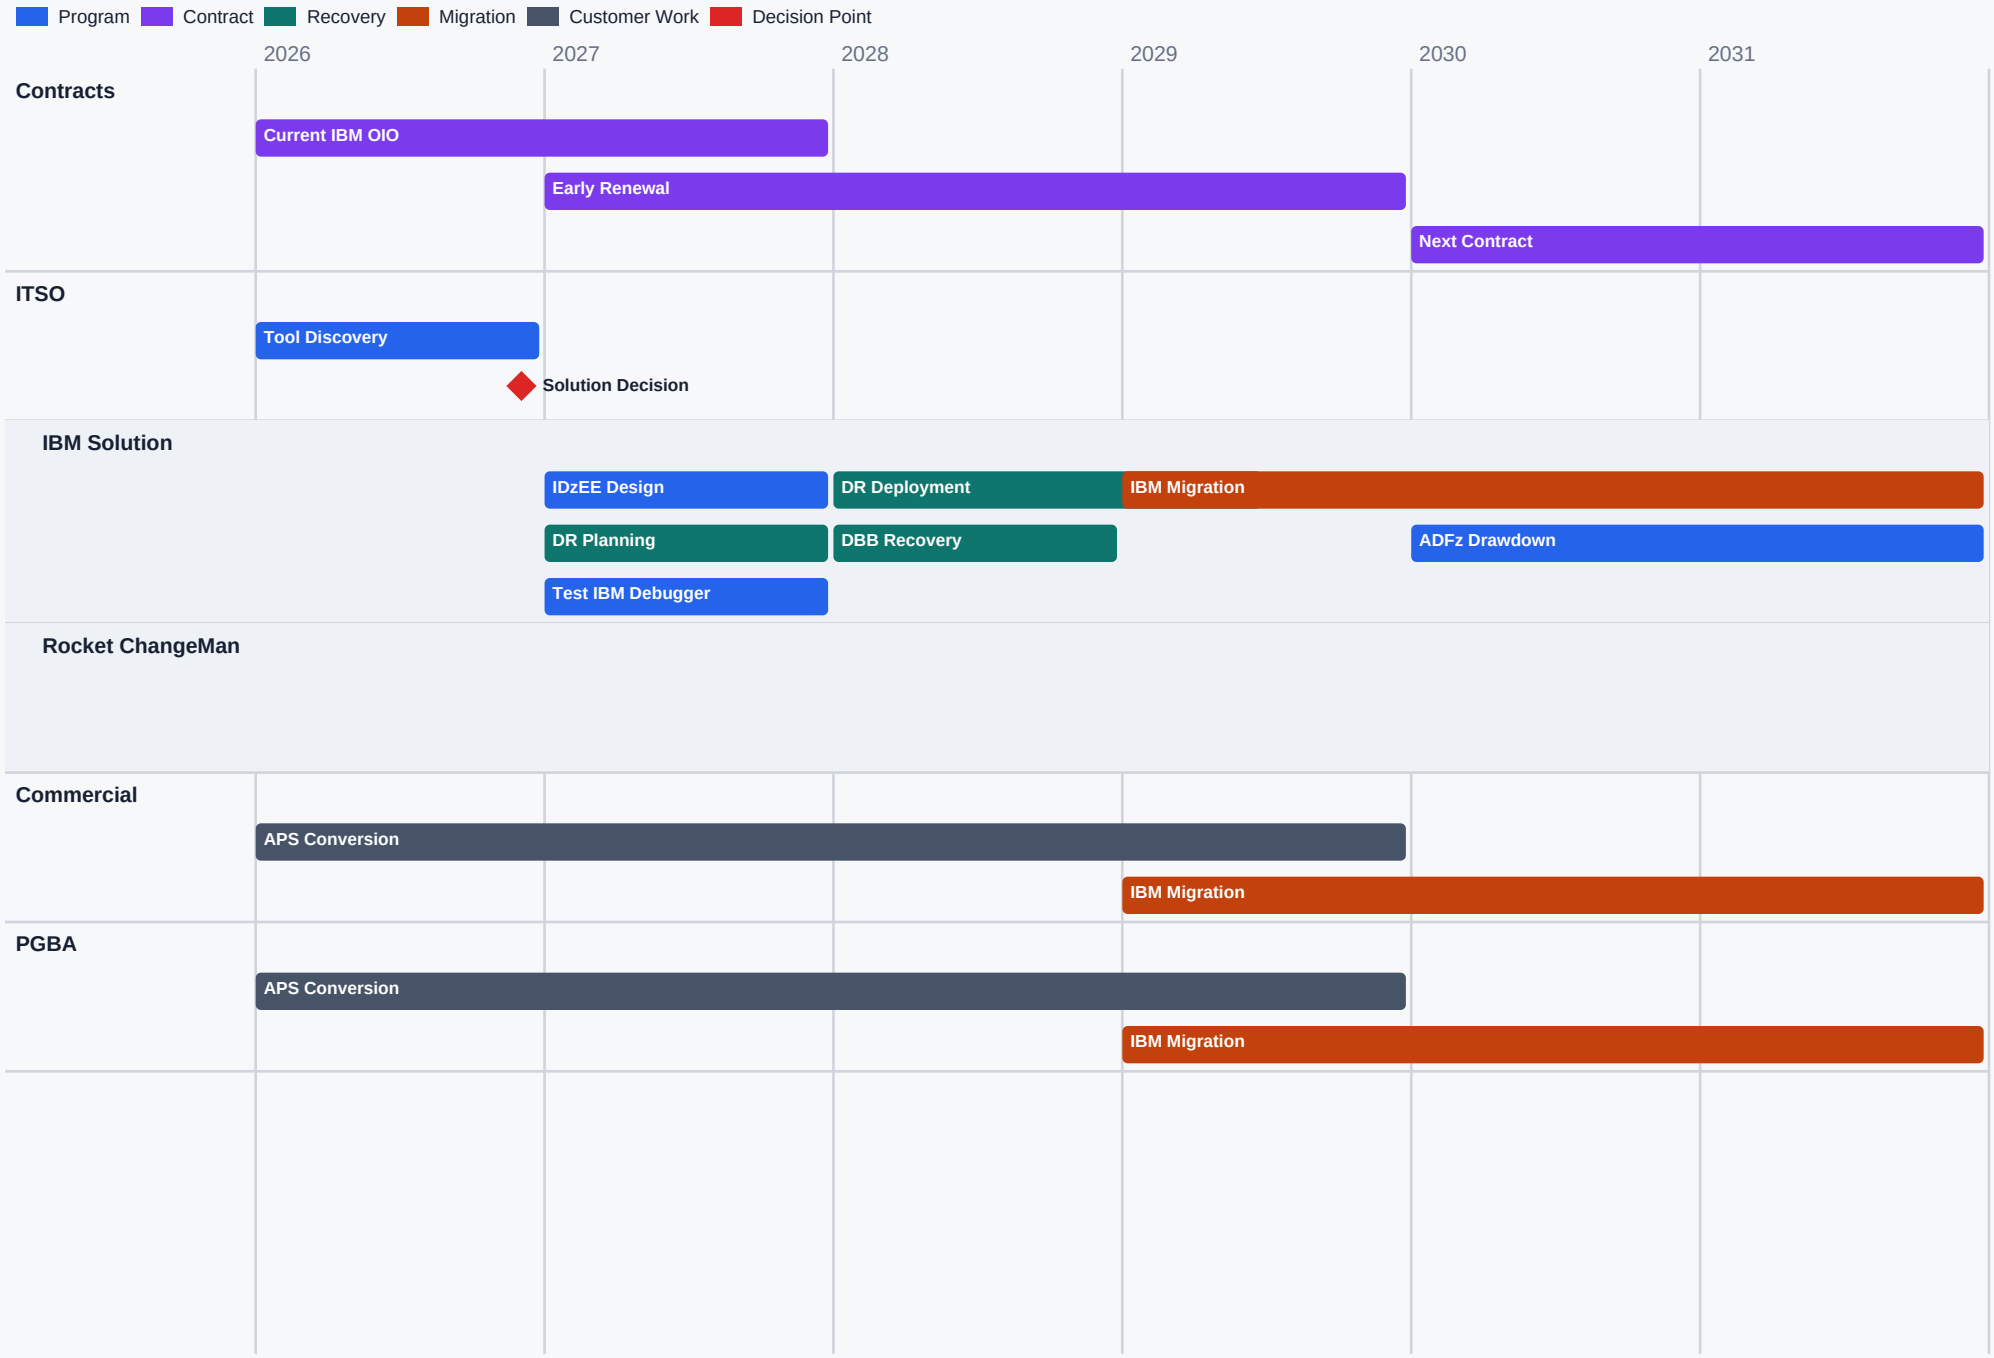

Decision-path view 1 - Only entries active for this path are shown.

Theme: executive

Path Details

Generated: 2026-09-15 08:16 AM Eastern Daylight Time
By: Mainframe Engineering

DECISION PATH Contract Path: Early renewal: 2027-2029 | Selected SDLC Solution: IBM suite viable

2026-2028 | Contracts | Contract | Current IBM OIO
Current IBM OIO term ends 01/01/2028.

2026-2027 | ITSO | Program | Tool Discovery
Tool discovery and IBM and Rocket proofs of concept conclude in 2026.

2026-2030 | Commercial | Customer Work | APS Conversion
Commercial APS conversion completes by the end of 2029.

2026-2030 | PGBA | Customer Work | APS Conversion
PGBA APS conversion completes by the end of 2029.

Decision at 2026.92 | ITSO | Decision Point | Solution Decision
Determine whether the IBM suite is viable; otherwise proceed with Rocket ChangeMan.

2027-2030 | Contracts | Contract | Early Renewal
Incentivized renewal runs 01/01/2027-12/31/2029.

2027-2028 | IBM Solution | Program | IDzEE Design
Pull down IDzEE, then configure, design, document, and plan the new SDLC in 2027.

2027-2028 | IBM Solution | Recovery | DR Planning
Design disaster recovery for GitHub, Artifactory, and DevOps Deploy.

2027-2028 | IBM Solution | Program | Test IBM Debugger
Evaluate IBM Debugger as the InterTest replacement.

2028-2029.5 | IBM Solution | Recovery | DR Deployment
Deploy distributed-tool disaster recovery and validate it during biannual exercises through mid-2029.

2028-2029 | IBM Solution | Recovery | DBB Recovery
Test mainframe DBB recovery and deploy the new SDLC lifecycle environments.

2029-2032 | IBM Solution | Migration | IBM Migration
Customers begin moving production-ready code into the IBM solution in 2029.

2029-2032 | Commercial | Migration | IBM Migration
Commercial begins moving production-ready code to the IBM solution in 2029.

2029-2032 | PGBA | Migration | IBM Migration
PGBA begins moving production-ready code to the IBM solution in 2029.

Path Details (continued)

Generated: 2026-09-15 08:16 AM Eastern Daylight Time
By: Mainframe Engineering

DECISION PATH Contract Path: Early renewal: 2027-2029 | Selected SDLC Solution: IBM suite viable

2030-2034 | Contracts | Contract | Next Contract

The early-renewal path requires another contract covering 2030-2033.

2030-2032 | IBM Solution | Program | ADFz Drawdown

Draw down ADFz in 2030 for File Manager, Fault Analyzer, and Application Performance Analyzer.

Written flow for the decision path shown above.

Mainframe SDLC Modernization Roadmap

Generated: 2026-09-15 08:16 AM Eastern Daylight Time
By: Mainframe Engineering

DECISION PATH Contract Path: Early renewal: 2027-2029 | Selected SDLC Solution: Rocket ChangeMan selected

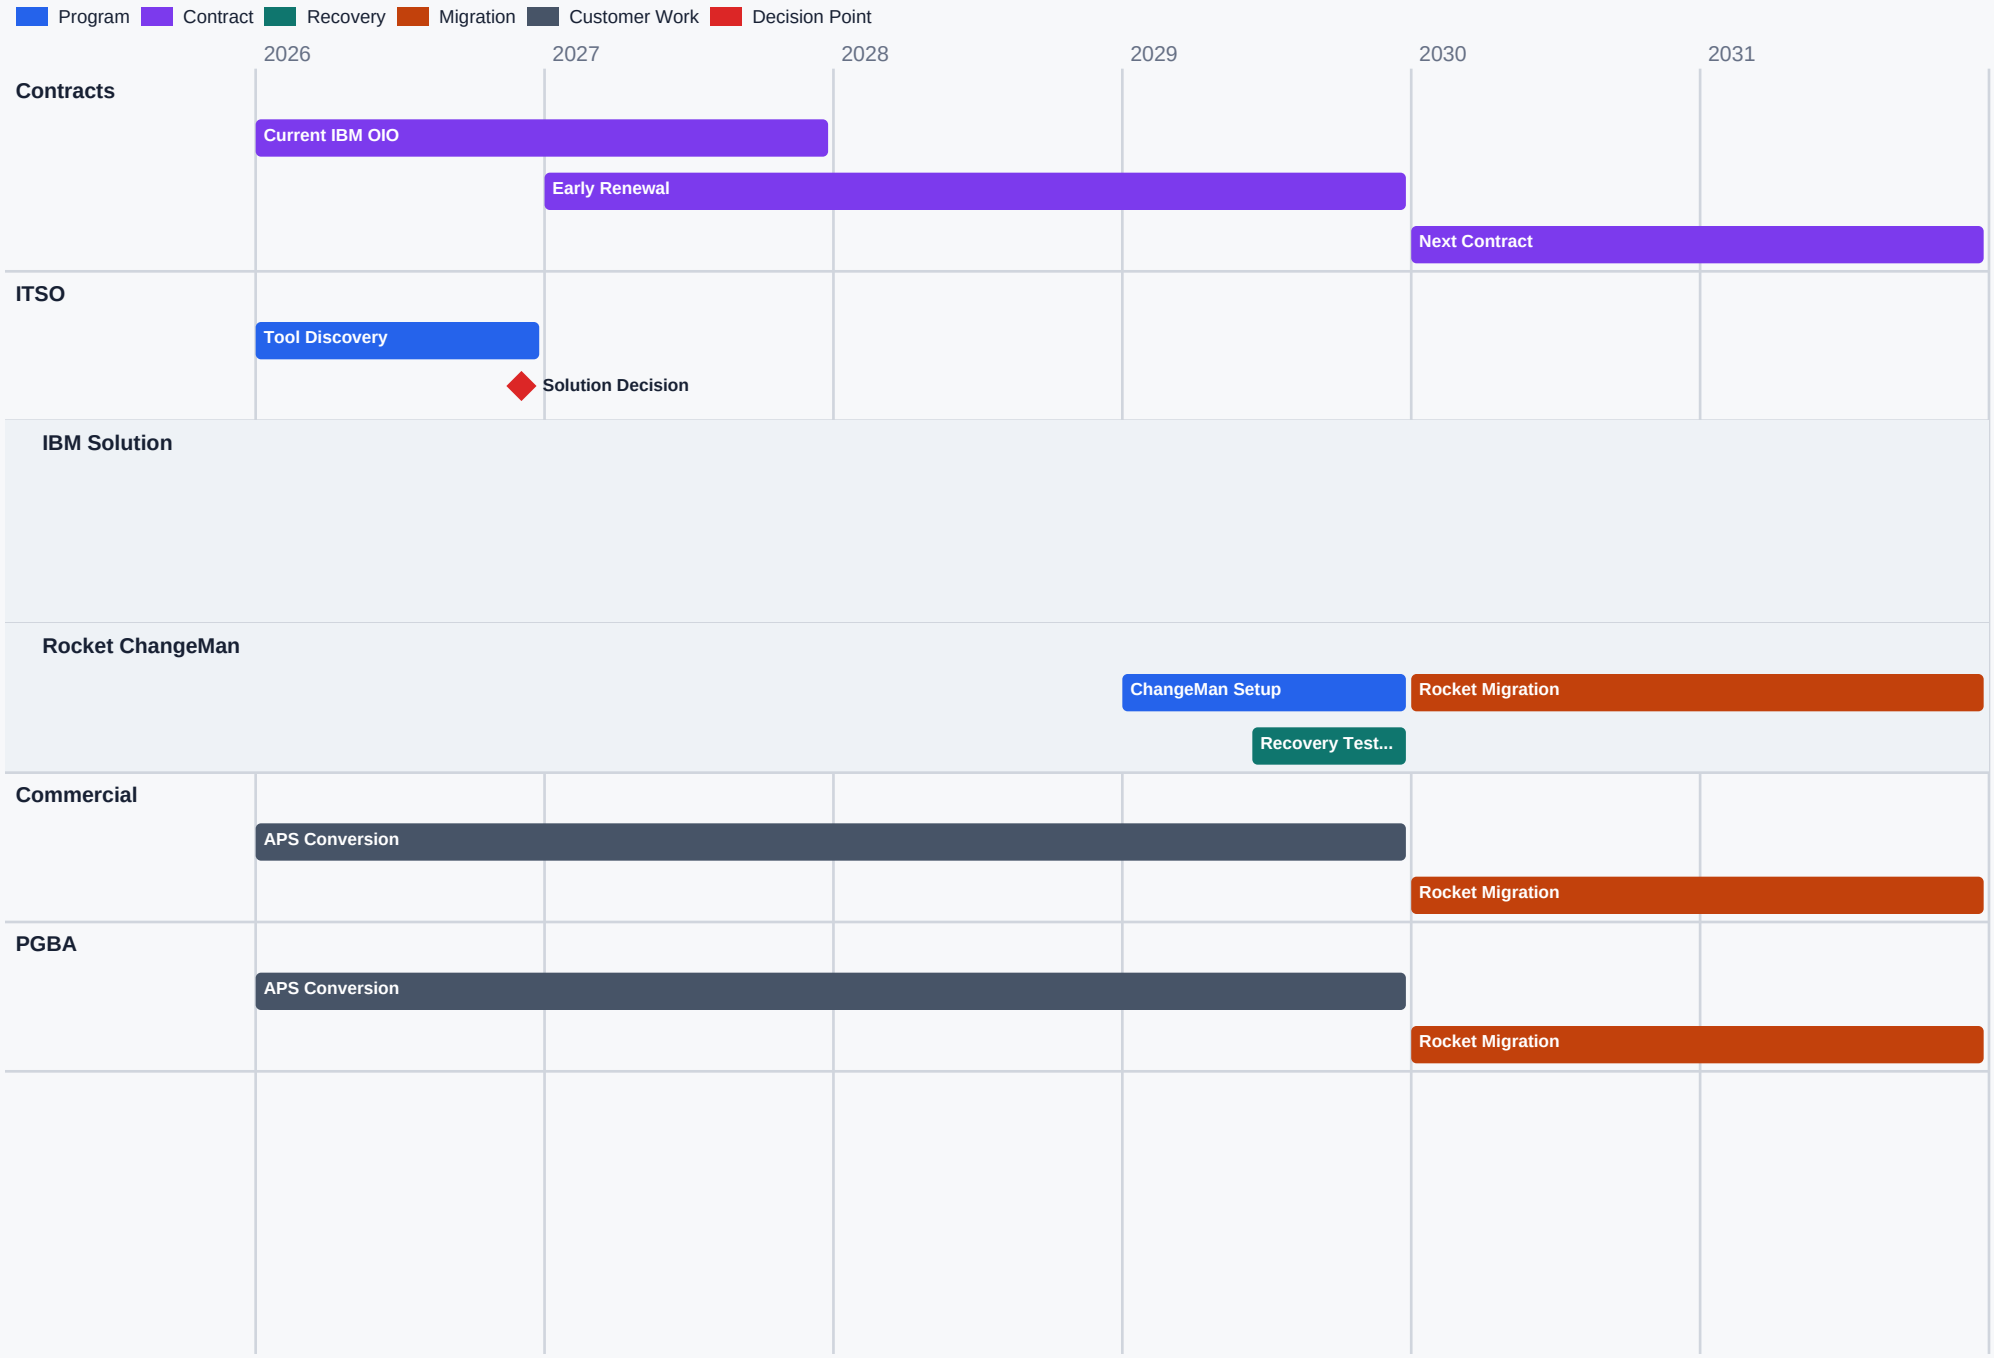

Decision-path view 2 - Only entries active for this path are shown.

Theme: executive

Path Details

Generated: 2026-09-15 08:16 AM Eastern Daylight Time
By: Mainframe Engineering

DECISION PATH Contract Path: Early renewal: 2027-2029 | Selected SDLC Solution: Rocket ChangeMan selected

2026-2028 | Contracts | Contract | Current IBM OIO
Current IBM OIO term ends 01/01/2028.

2026-2027 | ITSO | Program | Tool Discovery
Tool discovery and IBM and Rocket proofs of concept conclude in 2026.

2026-2030 | Commercial | Customer Work | APS Conversion
Commercial APS conversion completes by the end of 2029.

2026-2030 | PGBA | Customer Work | APS Conversion
PGBA APS conversion completes by the end of 2029.

Decision at 2026.92 | ITSO | Decision Point | Solution Decision
Determine whether the IBM suite is viable; otherwise proceed with Rocket ChangeMan.

2027-2030 | Contracts | Contract | Early Renewal
Incentivized renewal runs 01/01/2027-12/31/2029.

2029-2030 | Rocket ChangeMan | Program | ChangeMan Setup
Begin ChangeMan development and setup in 2029.

2029.45-2030 | Rocket ChangeMan | Recovery | Recovery Testing
Conduct ChangeMan recovery tests in 2029.

2030-2034 | Contracts | Contract | Next Contract
The early-renewal path requires another contract covering 2030-2033.

2030-2032 | Rocket ChangeMan | Migration | Rocket Migration
Customers begin moving code to ChangeMan in 2030.

2030-2032 | Commercial | Migration | Rocket Migration
Commercial begins moving production-ready code to Rocket ChangeMan in 2030.

2030-2032 | PGBA | Migration | Rocket Migration
PGBA begins moving production-ready code to Rocket ChangeMan in 2030.

Written flow for the decision path shown above.

Mainframe SDLC Modernization Roadmap

Generated: 2026-09-15 08:16 AM Eastern Daylight Time
By: Mainframe Engineering

DECISION PATH Contract Path: Current term, then 2028-2030 | Selected SDLC Solution: IBM suite viable

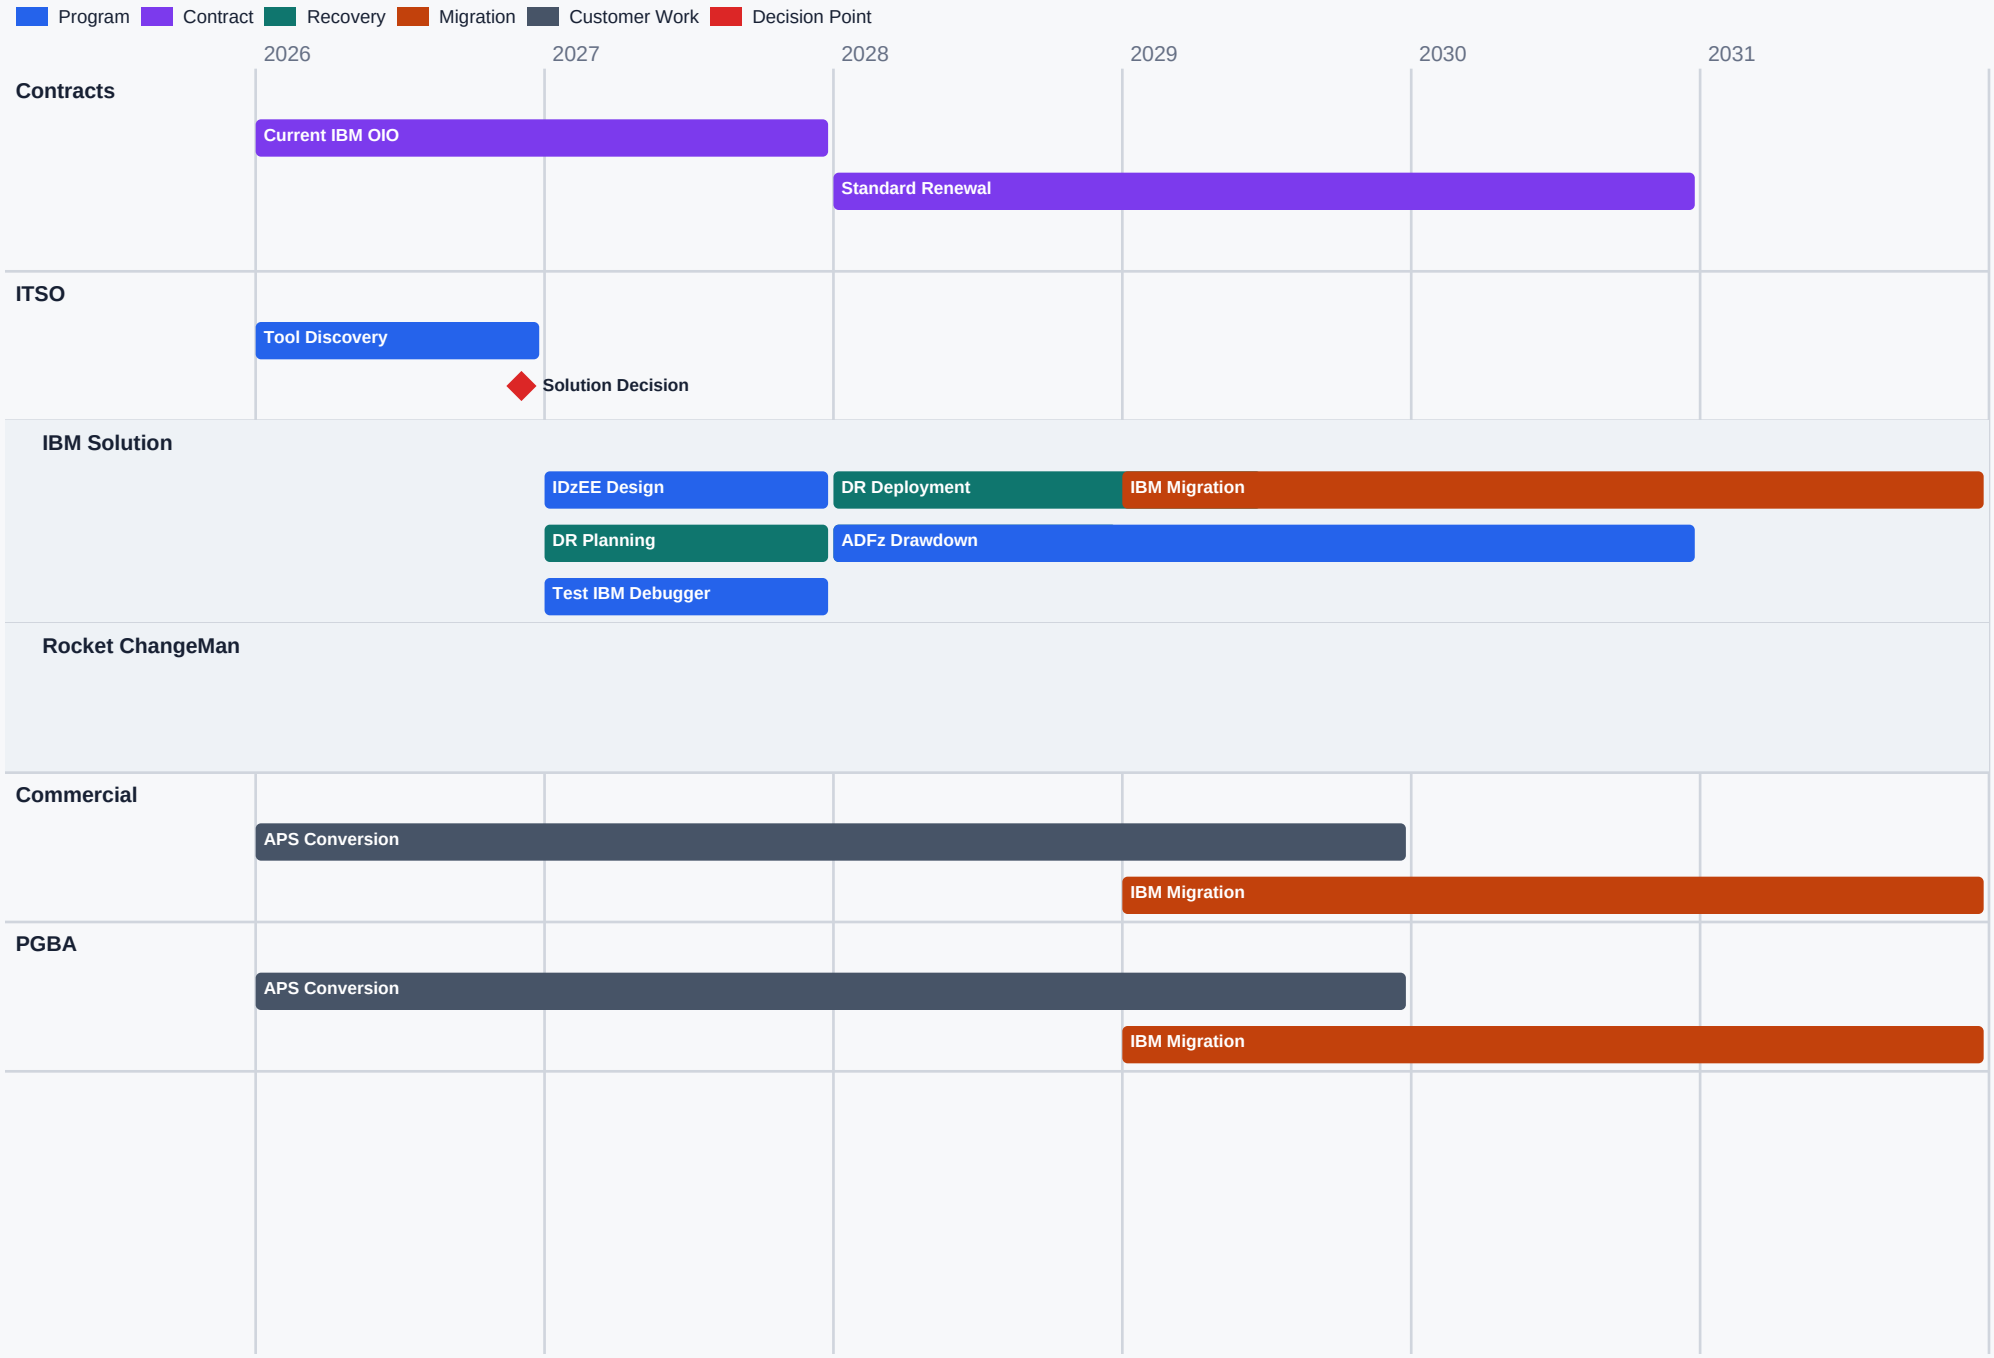

Decision-path view 3 - Only entries active for this path are shown.

Theme: executive

Path Details

Generated: 2026-09-15 08:16 AM Eastern Daylight Time
By: Mainframe Engineering

DECISION PATH Contract Path: Current term, then 2028-2030 | Selected SDLC Solution: IBM suite viable

2026-2028 | Contracts | Contract | Current IBM OIO
Current IBM OIO term ends 01/01/2028.

2026-2027 | ITSO | Program | Tool Discovery
Tool discovery and IBM and Rocket proofs of concept conclude in 2026.

2026-2030 | Commercial | Customer Work | APS Conversion
Commercial APS conversion completes by the end of 2029.

2026-2030 | PGBA | Customer Work | APS Conversion
PGBA APS conversion completes by the end of 2029.

Decision at 2026.92 | ITSO | Decision Point | Solution Decision
Determine whether the IBM suite is viable; otherwise proceed with Rocket ChangeMan.

2027-2028 | IBM Solution | Program | IDzEE Design
Pull down IDzEE, then configure, design, document, and plan the new SDLC in 2027.

2027-2028 | IBM Solution | Recovery | DR Planning
Design disaster recovery for GitHub, Artifactory, and DevOps Deploy.

2027-2028 | IBM Solution | Program | Test IBM Debugger
Evaluate IBM Debugger as the InterTest replacement.

2028-2031 | Contracts | Contract | Standard Renewal
If early incentives are not compelling, renew for 2028-2030.

2028-2029.5 | IBM Solution | Recovery | DR Deployment
Deploy distributed-tool disaster recovery and validate it during biannual exercises through mid-2029.

2028-2029 | IBM Solution | Recovery | DBB Recovery
Test mainframe DBB recovery and deploy the new SDLC lifecycle environments.

2028-2031 | IBM Solution | Program | ADFz Drawdown
Without early renewal, draw down ADFz during the 2028-2030 contract term.

2029-2032 | IBM Solution | Migration | IBM Migration
Customers begin moving production-ready code into the IBM solution in 2029.

2029-2032 | Commercial | Migration | IBM Migration
Commercial begins moving production-ready code to the IBM solution in 2029.

Path Details (continued)

Generated: 2026-09-15 08:16 AM Eastern Daylight Time
By: Mainframe Engineering

DECISION PATH Contract Path: Current term, then 2028-2030 | Selected SDLC Solution: IBM suite viable

2029-2032 | PGBA | Migration | IBM Migration

PGBA begins moving production-ready code to the IBM solution in 2029.

Written flow for the decision path shown above.

Mainframe SDLC Modernization Roadmap

Generated: 2026-09-15 08:16 AM Eastern Daylight Time
By: Mainframe Engineering

DECISION PATH Contract Path: Current term, then 2028-2030 | Selected SDLC Solution: Rocket ChangeMan selected

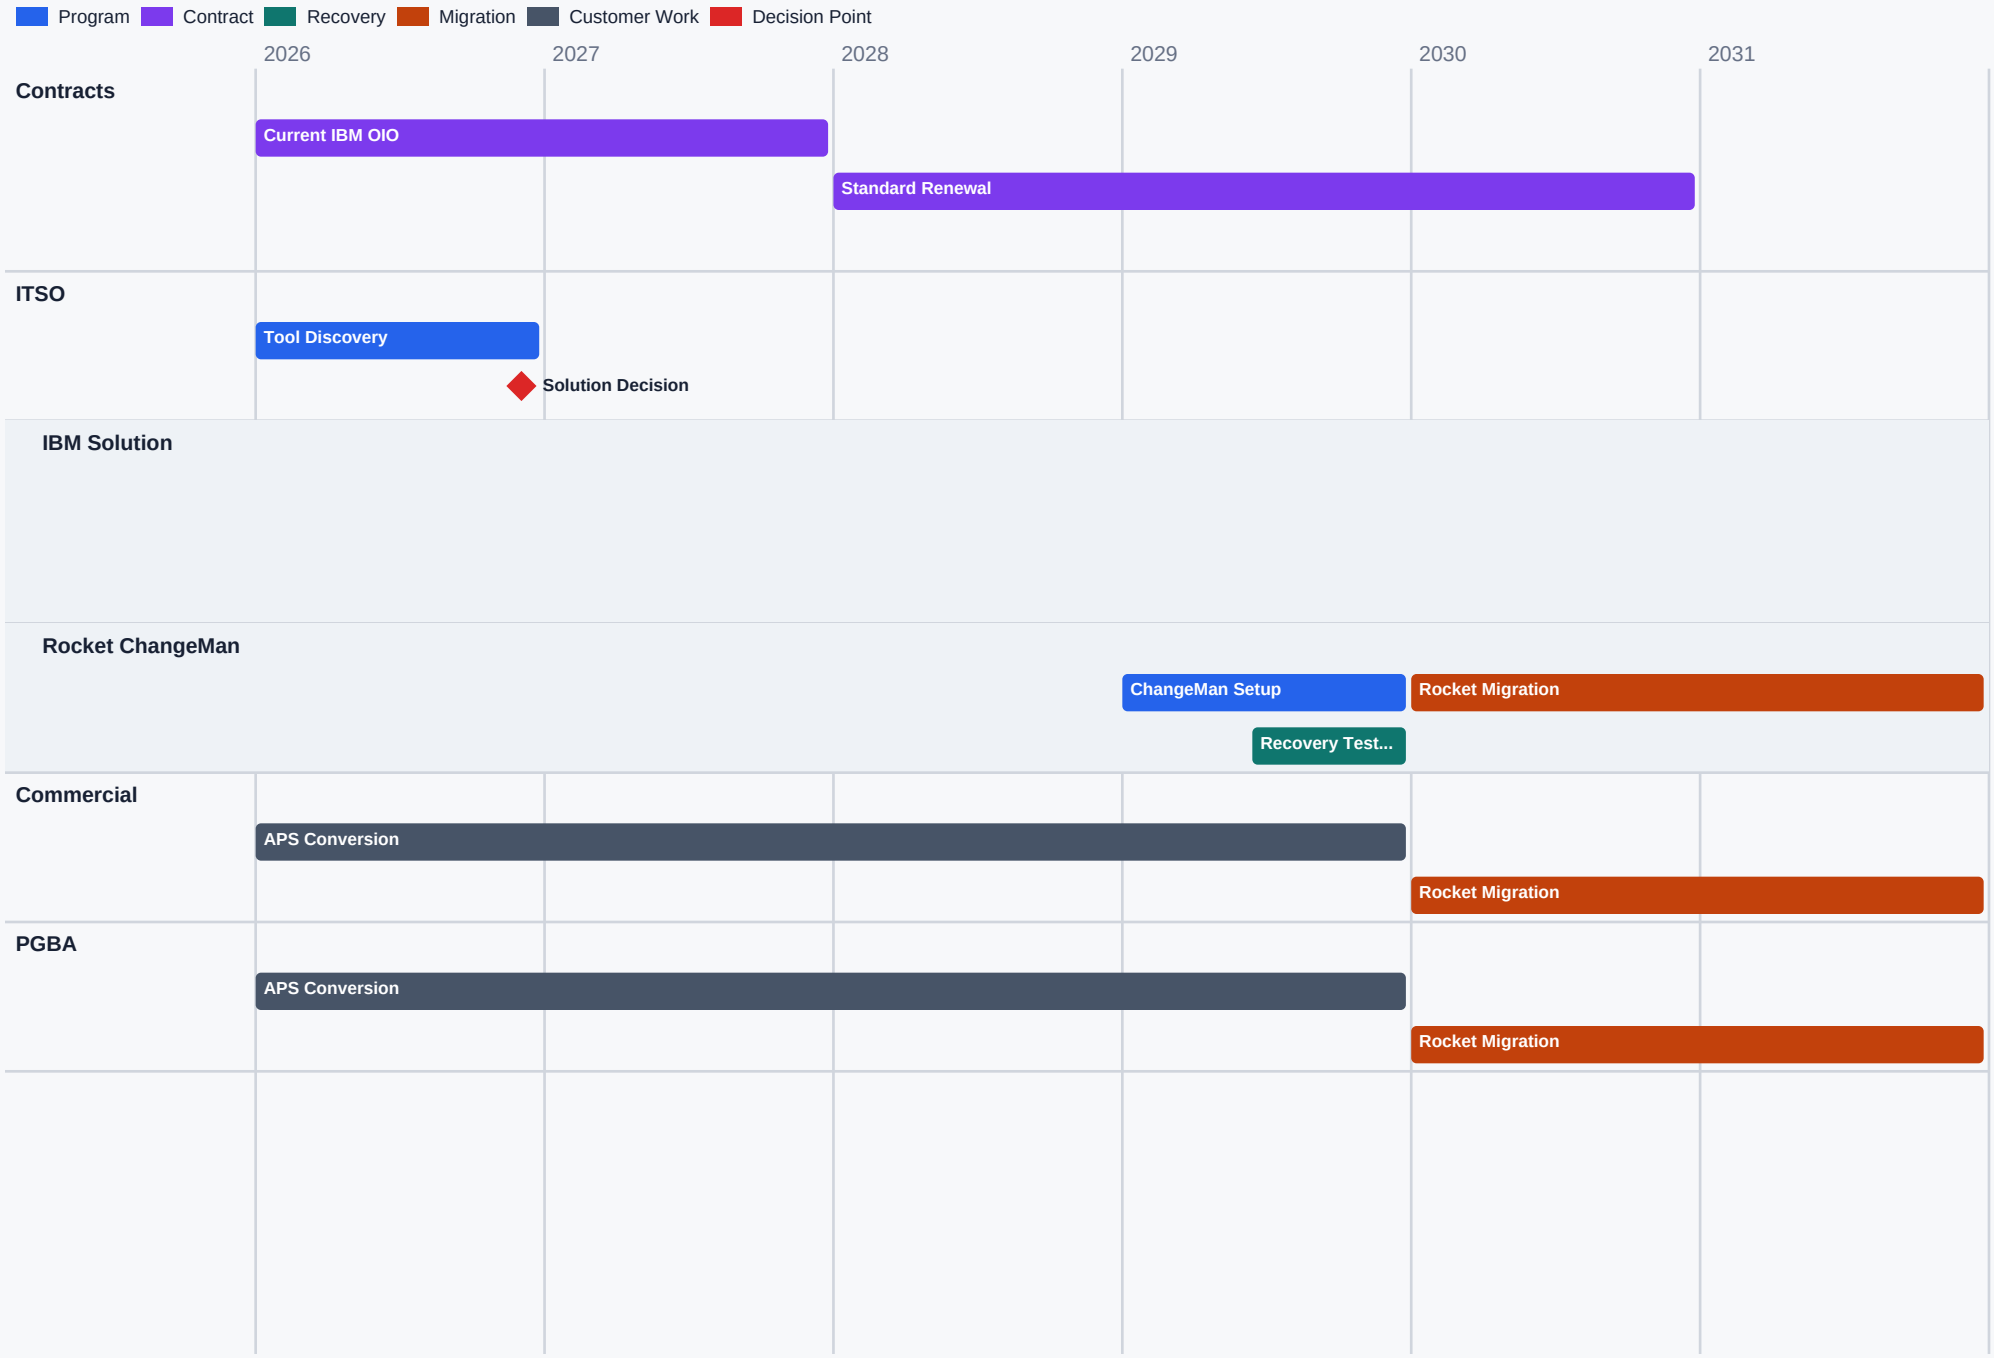

Decision-path view 4 - Only entries active for this path are shown.

Theme: executive

Path Details

Generated: 2026-09-15 08:16 AM Eastern Daylight Time
By: Mainframe Engineering

DECISION PATH Contract Path: Current term, then 2028-2030 | Selected SDLC Solution: Rocket ChangeMan selected

2026-2028 | Contracts | Contract | Current IBM OIO
Current IBM OIO term ends 01/01/2028.

2026-2027 | ITSO | Program | Tool Discovery
Tool discovery and IBM and Rocket proofs of concept conclude in 2026.

2026-2030 | Commercial | Customer Work | APS Conversion
Commercial APS conversion completes by the end of 2029.

2026-2030 | PGBA | Customer Work | APS Conversion
PGBA APS conversion completes by the end of 2029.

Decision at 2026.92 | ITSO | Decision Point | Solution Decision
Determine whether the IBM suite is viable; otherwise proceed with Rocket ChangeMan.

2028-2031 | Contracts | Contract | Standard Renewal
If early incentives are not compelling, renew for 2028-2030.

2029-2030 | Rocket ChangeMan | Program | ChangeMan Setup
Begin ChangeMan development and setup in 2029.

2029.45-2030 | Rocket ChangeMan | Recovery | Recovery Testing
Conduct ChangeMan recovery tests in 2029.

2030-2032 | Rocket ChangeMan | Migration | Rocket Migration
Customers begin moving code to ChangeMan in 2030.

2030-2032 | Commercial | Migration | Rocket Migration
Commercial begins moving production-ready code to Rocket ChangeMan in 2030.

2030-2032 | PGBA | Migration | Rocket Migration
PGBA begins moving production-ready code to Rocket ChangeMan in 2030.

Written flow for the decision path shown above.
